

25X1A5a2


To:

Oct. 13, 1959

From: Clarence L. Johnson

Subject: PROJECT MEMO - PRODUCTION SCHEDULE, A-12

Because of engine changes and configuration problems, the first flight will be 20 months from go-ahead. All 12 airplanes will, however, be done in 36 months.

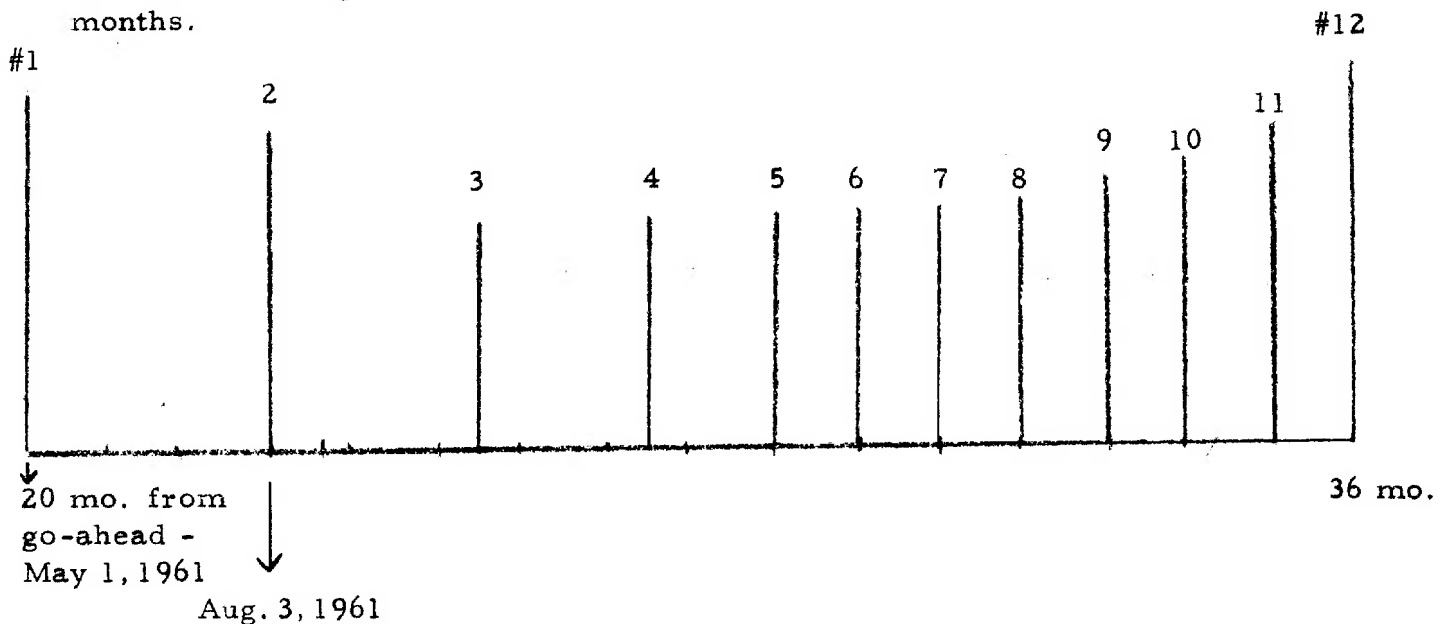

25X1A6a

Delivery to Customer at [REDACTED] 25X1A6a

Have to deliver aircraft to [REDACTED] approximately one month prior to above dates to provide time for re-assembly and production test.

#1 May 1, 1961	#5 Feb. 7, 1962	#9 June 13, 1962
#2 Aug. 3, 1961	#6 Mar. 7, 1962	#10 July 11, 1962
#3 Oct. 18, 1961	#7 Apr. 11, 1962	#11 Aug. 10, 1962
#4 Dec. 20, 1961	#8 May 11, 1962	#12 Sept. 5, 1962

FOIAb6 [REDACTED]

Clarence L. Johnson

Vice President

Advanced Development Projects

CLJ:vmg
